

REPORTING PERIOD

July 2026

PROGRAMME DATA DATE

23 Jul 2026

REPORT DATE

25 Aug 2026

PRESENTED BY

Henry Corcoran

REMIT

Design, Commercial & Procurement

OVERALL ASSESSMENT

 **GREEN**

Schedule performance is **7.9 points behind plan** and forecast to recover next period — the July slip sits on M140 and M145 C01 issue and carries no impact to the procurement programme. Forecast at completion rose **€602k** on the Dublin Airport advanced works instruction and four smaller changes. Open Early Warnings fell by **seven**, and approved change value is **unmoved**.

01 — POSITION


Where the programme stands

MOVEMENT SHOWN VS JUNE 2026

SCHEDULE PROGRESS 49.2% ▼ 7.9 pts vs plan	FORECAST AT COMPLETION €45.34M ▲ €602k · +1.3%	APPROVED CHANGE VALUE €11.72M ● No movement
OPEN EARLY WARNINGS 22 ▼ 7 closed out	TEAM SIZE 97 FTE ▲ 4 on period	MAJOR & KEY RISKS 9 ● High · no change

Milestone completion against plan

63 MILESTONES IN SCOPE




COMPLETE	ON TRACK	BEHIND	AT RISK
32	15	16	0


July result — five of nine milestones achieved. The four deferred milestones are M140 and M145 C01 Package Issue and Ready for Tender, held pending client acceptance of the submitted package. Impact is 20 working days on C01 issue, moving it from 09 Jul to 07 Aug. **No impact to the procurement programme** — both packages remain ahead of the 18 Sep ITT date.

02 – KEY DATES

Milestone track to November 2026

FORECAST POSITIONS AT DATA DATE 23 JUL 2026

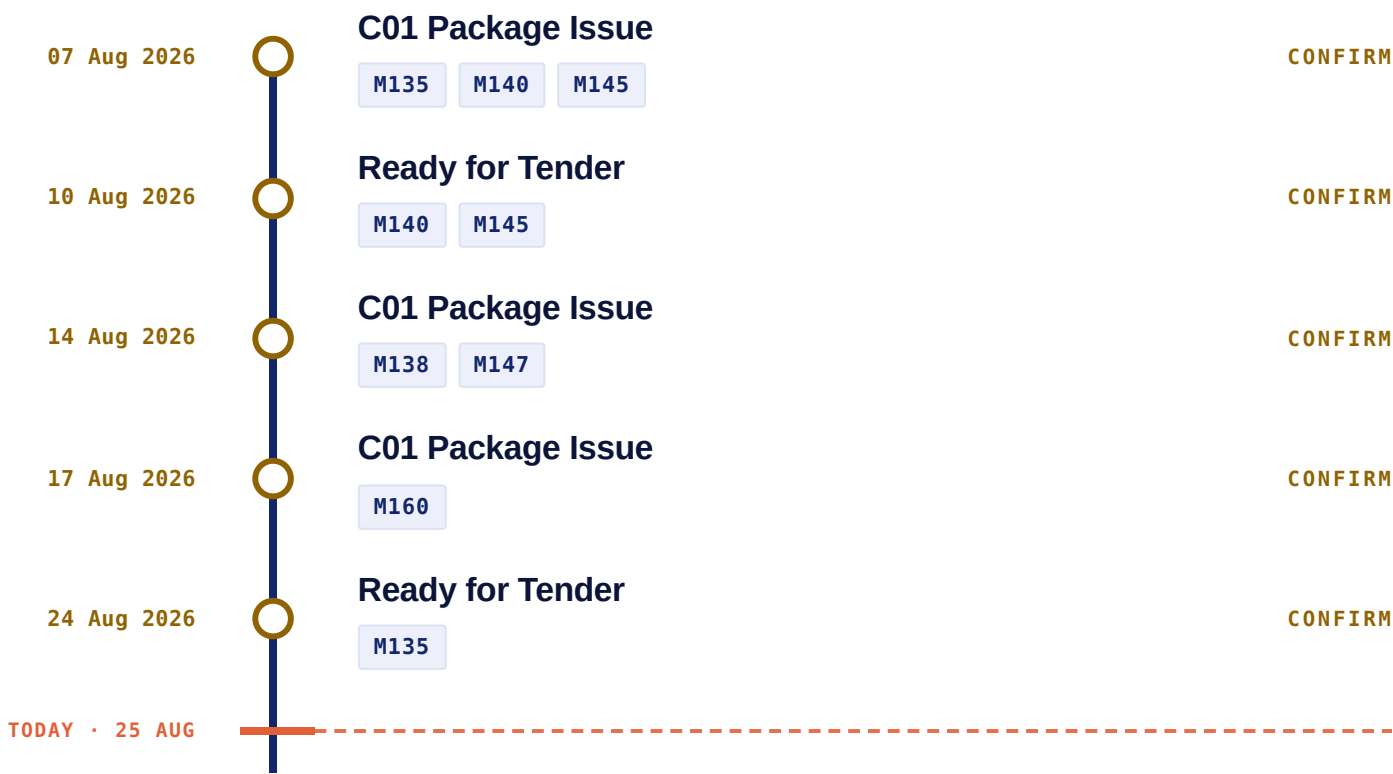

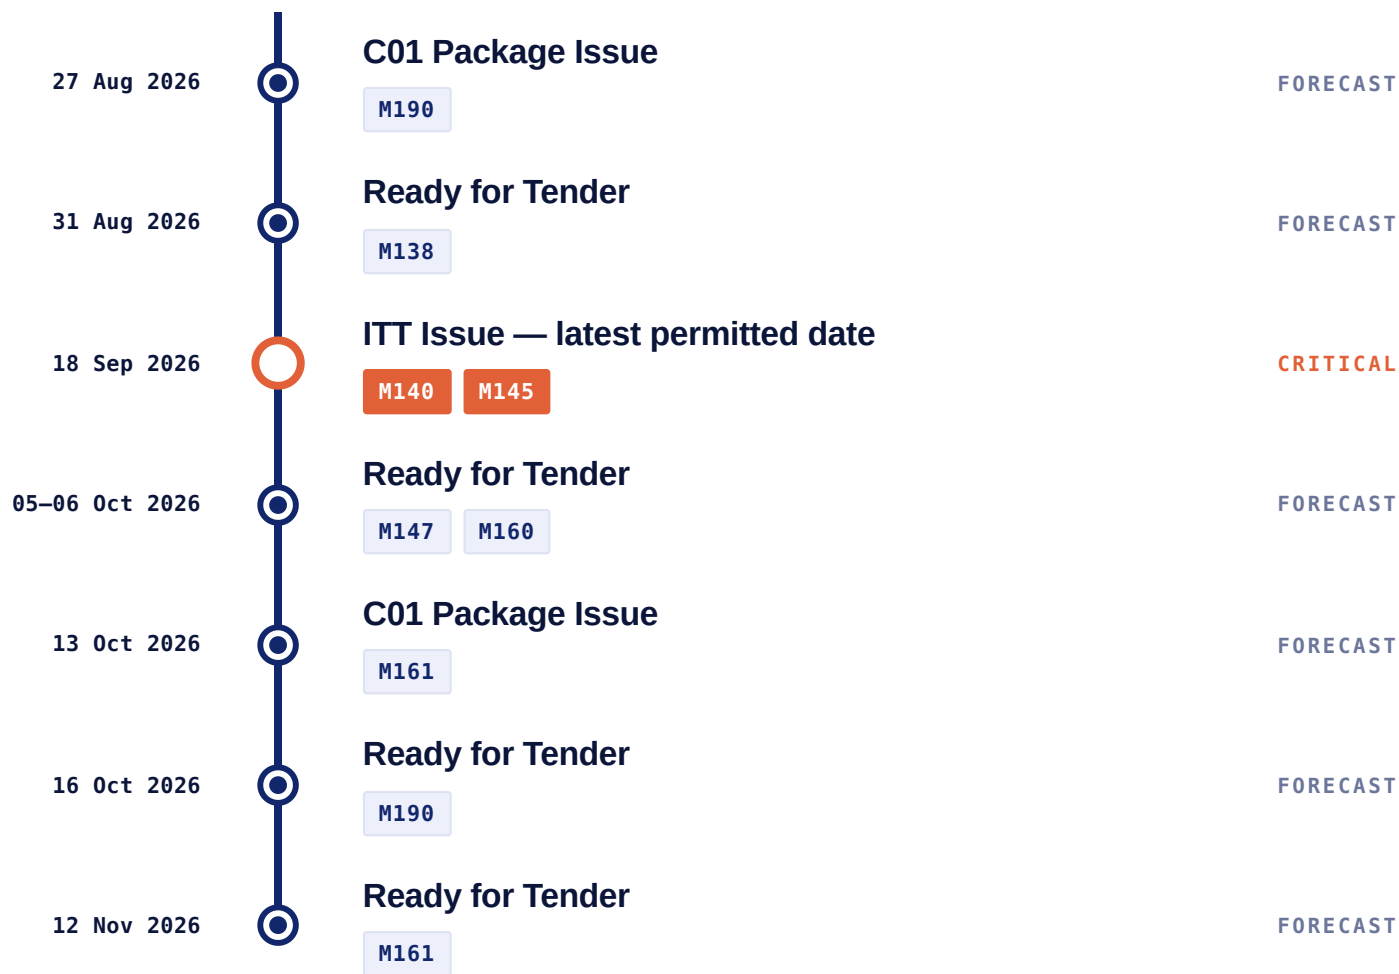

HORIZON – NORTHERN UTILITIES PACKAGES				
PACKAGE	IDC	C01 PACKAGE ISSUE	READY FOR TENDER	MOVEMENT IN PERIOD
M141	06 Aug 2026	18 Dec 2026	18 Jan 2027	No movement
M142	19 Aug 2026	14 Jan 2027	29 Jan 2027	No movement
M146	02 Sep 2026	28 Jan 2027	15 Feb 2027	No movement

Design, Commercial & Procurement

MOVEMENT IN PERIOD AND NEXT ACTIONS

Design	Commercial	Procurement
PROGRESSING – UTILITIES PACING	FORECAST UP €602K	NEC CONVERSION DRIVING REWORK
● M135 IDC formally waived by TII. DOSEC approval received, CEMPs reissued, documents under MetroLink technical review. Instruction to proceed to C01 expected. ● M138 Advancing through assurance on a mini-IDC agreed with TII; CEMPs circa 80% reviewed — but proceeding without full land access information. ● M147 Carbon and Dust CEMPs submitted; review comments received 23 Jul. Survey delays now threaten the two-track delivery approach. ● M141 · M142 · M146 In pre-IDC development. Utility inputs are the pacing item on all three. ● M145 Watch — road configuration change, a possible piled retaining wall and Utility Day-1 changes all carry design and cost impact.	● EAC now €45.34M, up €602k on the period — 88% of that is the new Dublin Airport advanced works design instruction. ● Approved change value flat at €11.72M. No new approvals landed in period; €5.40M sits pending in CEMAR. ● Early warnings down seven to 22 open. Fifteen requested to close and a further seven close on instruction. ● One change notice raised — CN-95 Planning Permission, Balheary. Four EWs raised (249–252); EW-251 already avoided. ● Watch — the BusConnects interface change on M140 and the emerging M145 scope both carry unpriced exposure.	● M130 In tender evaluation. Commercial assessments complete, but the Tender Evaluation Report has slipped from July and reviewer dates are unconfirmed. Design Certificate outstanding. ● M190 NEC Option A confirmed. Price list and task order schedule being reconverted; PQQ tender period extension requested. ● M160 NEC contract conversion continues alongside PQQ and ITT preparation — the form change is creating assurance uncertainty. ● M140 · M145 Remain on track to issue ahead of the 18 Sep ITT date despite the 20-day C01 slip. ● M200 Framework scoped as seven lots. Schedule of rates and scoping documents still to be developed.

Contract position and change movement

ALL FIGURES EX-VAT

ORIGINAL CONTRACT	APPROVED TO DATE	PENDING IN CEMAR	PROPOSED ESTIMATE	ANTICIPATED TOTAL
€21.39M	€33.11M	€5.40M	€6.83M	€45.34M
Baseline	Incl. €11.72M change		Notified changes	

		Issued, not approved		Forecast at completion
--	--	----------------------	--	------------------------

FORECAST MOVEMENT IN PERIOD – €44.74M TO €45.34M		
REFERENCE	DRIVER	VALUE
CN-93	Detailed design, Dublin Airport advanced works — new instruction, estimated fee value	€400,000
CN-77	Additional planner for the consents workstream — forecast to end 2027	€97,500
CN-031	CEMPs — additional effort on the northern contracts	€40,000
CN-047	Archaeological de-risking — design finalisation for M145 submission	€38,000
CN-035	ESB planning application — landscape services and site notice erection	€26,980
	Total movement on period	€602,480

Early warning pipeline — 252 raised to date. 208 avoided or passed, 15 requested to close, 7 close once change is instructed, leaving **22 open**. Four were raised this period: commitments baseline information (EW-249), the Dardistown station box and Northwood foul network diversion (EW-250), extended Uisce Éireann engagement (EW-251, avoided) and issuance of utility design models for coordination (EW-252).

Resourcing — 97 FTE, up 4 on the period. Split is 61 design, 25 management and 11 procurement. Carolyn Boykiw joined as Project Manager and Andria Robson as Planner for the consents workstream, with Marco Trabacca onboarded as a graduate. The uplift is driven by pre-commencement surveys, ground movement analysis and M14X technical evaluations. **A summer dip is anticipated** on annual leave against a heavy August deliverable load.

Top five programme risks

9 MAJOR & KEY · NO CHANGE ON PERIOD

SCORE	RISK	PACKAGE	POSITION
25	Delays due to vacant possession TII-004	All	Agreements with third parties may not be reached, requiring enforcement of rights of entry. Ownership matrix and land access schedule being confirmed with TII.
24	Programme interface delays PR-005	All	Delay in one package cascades across the others. Interface register maintained fortnightly; coordination meetings proposed as a contractual requirement.
22	Condition of utility assets 110	All	Assets may need upgrade before diversion. Targeted slit trenching underway ahead of procurement; residual risk to pass formally to construction.
22	ESB resources and inputs delayed ML-UTL-A-R10017	All	ESB may not resource connections and diversions to programme. Early formal engagement in train; float being built around ESB-dependent activities.
22	Heritage removal more onerous than anticipated TII-024	M140	Burial site removal may be more complex, or further sites found. Specialist archaeologists engaged; escalation path agreed with the National Monuments Service.

Decisions required from leadership

Four decisions needed to hold the September and October dates

Each of these sits outside the AWDS team's control and is currently absorbing float.

01

M142 recovery plan and resources

Approval of the recovery plan and the additional resources it requires, ahead of the 19 Aug IDC.

02

ESB and Uisce Éireann interfaces

Confirmation of ESB diversion dates and the Uisce Éireann interface positions. Two of the top five risks depend on this.

03

Land access information

M138 is proceeding to assurance without full land access constraint information and M146 utility delays threaten IDC readiness. Confirm the route to that information, or accept the design assumption risk.

04

M130 evaluation and Design Certificate

Confirm the review team and procurement evaluation dates, and the route for Design Certificate issue, so the Tender Evaluation Report can be closed out.

Where the team is pointed

NEXT 30 DAYS

Aug	Issue C01 packages for M135, M138, M140, M145 and M147.	06–19 Aug	Start IDCs on the Northern Utilities contracts — M141 and M142.
27–31 Aug	M190 C01 package issue and M138 ready for tender .	Ongoing	Continue critical path recovery on M140 and M145 and progress land access .
18 Sep	Hold M140 and M145 to the ITT issue date — the binding procurement constraint this quarter.	Ongoing	Close out the NEC conversion on M160 and M190 and settle assurance requirements under the new form.
